

November 29, 2013

REQUEST FOR PROPOSAL "RFP" No. PS20130786
MOVE CONSULTANT & MOVE SERVICES FOR TENANT RELOCATION

ADDENDUM NO. 1

RE: PROPOSED PROJECT SCHEDULES

PLEASE ADD:

See attached project schedules for 814 Richards Street, 507 West Broadway and 515 West 10th Avenue.

This addendum must be completed, and attached to your Proposal form.

If you have already submitted your Tender, this amendment shall be submitted to the Purchasing Services Office, City of Vancouver, 453 West 12th Avenue, Vancouver, British Columbia, Canada, V5Y 1V4, (Courier Delivery and Drop off is at the Information Desk, Main Floor Rotunda of the same address), prior to the Closing Time: 3:00:00 pm Local Vancouver, BC Time, December 12, 2013 in an envelope clearly marked "ADDENDUM No. 1 to RFP No. PS20130786 MOVE CONSULTANT & MOVE SERVICES FOR TENANT RELOCATION".

NAME OF VENDOR

SIGNATURE OF AUTHORIZED SIGNATORY

DATE

Alison Hall
Contracting Specialist


Act ID	Description	Orig Dur	Early Start	Early Finish	2013				2014									
					SEP	OCT	NOV	DEC	JAN	FEB	MAR	APR	MAY					
SC	Overall Construction Project	18w *	23OCT13	06MAR14														
1.0	Pre-Construction	4w2d *	23OCT13	22NOV13														
1.1	Contract Award	1d	23OCT13	23OCT13														
1.15	Building Permit Issued	0	12NOV13															
1.2	Mobilize on Site	1w	18NOV13	22NOV13														
2.0	Building Construction	14w *	18NOV13	03MAR14														
2.1	Area 1 -- 4th Floor North	9w *	18NOV13 *	24JAN14														
2.1.10	Selective Demolition	1w	18NOV13	22NOV13														
2.1.20	Electrical/Data Rough-in	1w	25NOV13 *	29NOV13														
2.1.30	Mechanical Rough-in	1w	25NOV13	29NOV13														
2.1.40	Steel Stud Framing	1w	02DEC13 *	06DEC13														
2.1.50	Drywall Finishing	1w	09DEC13	13DEC13														
2.1.60	Architectural Finishes	3w	16DEC13	10JAN14														
2.1.70	Mechanical Finishes	3w	16DEC13	10JAN14														
2.1.80	Electrical Finishes	3w	16DEC13	10JAN14														
2.1.90	Furniture Installation	2w	13JAN14	24JAN14														
2.2	Area 2 -- 3rd Floor South	8w *	25NOV13	24JAN14														
2.2.10	Selective Demolition	1w	25NOV13	29NOV13														
2.2.20	Electrical/Data Rough-in	1w	02DEC13 *	06DEC13														
2.2.30	Mechanical Rough-in	1w	02DEC13	06DEC13														
2.2.40	Steel Stud Framing	1w	09DEC13 *	13DEC13														
2.2.50	Drywall Finishing	1w	16DEC13	20DEC13														
2.2.60	Architectural Finishes	2w	23DEC13	10JAN14														
2.2.70	Mechanical Finishes	2w	23DEC13	10JAN14														
2.2.80	Electrical Finishes	2w	23DEC13	10JAN14														
2.2.90	Furniture Installation	2w	13JAN14	24JAN14														
2.3	Area 3 -- 3rd Floor North	8w *	02DEC13	31JAN14														
2.3.10	Selective Demolition	1w	02DEC13	06DEC13														
2.3.20	Electrical/Data Rough-in	1w	09DEC13 *	13DEC13														
2.3.30	Mechanical Rough-in	1w	09DEC13	13DEC13														
2.3.40	Steel Stud Framing	1w	16DEC13 *	20DEC13														

Start date	23OCT13
Finish date	06MAR14
Data date	23OCT13
Run date	21NOV13
Page number	1A
© Primavera Systems, Inc.	

**814 Richards Street
Bynett Construction Services Ltd.**

- Early bar
- Progress bar
- Critical bar
- Summary bar
- Start milestone point
- Finish milestone point


COV CROSSROADS Office Renovation BASELINE SCHEDULE

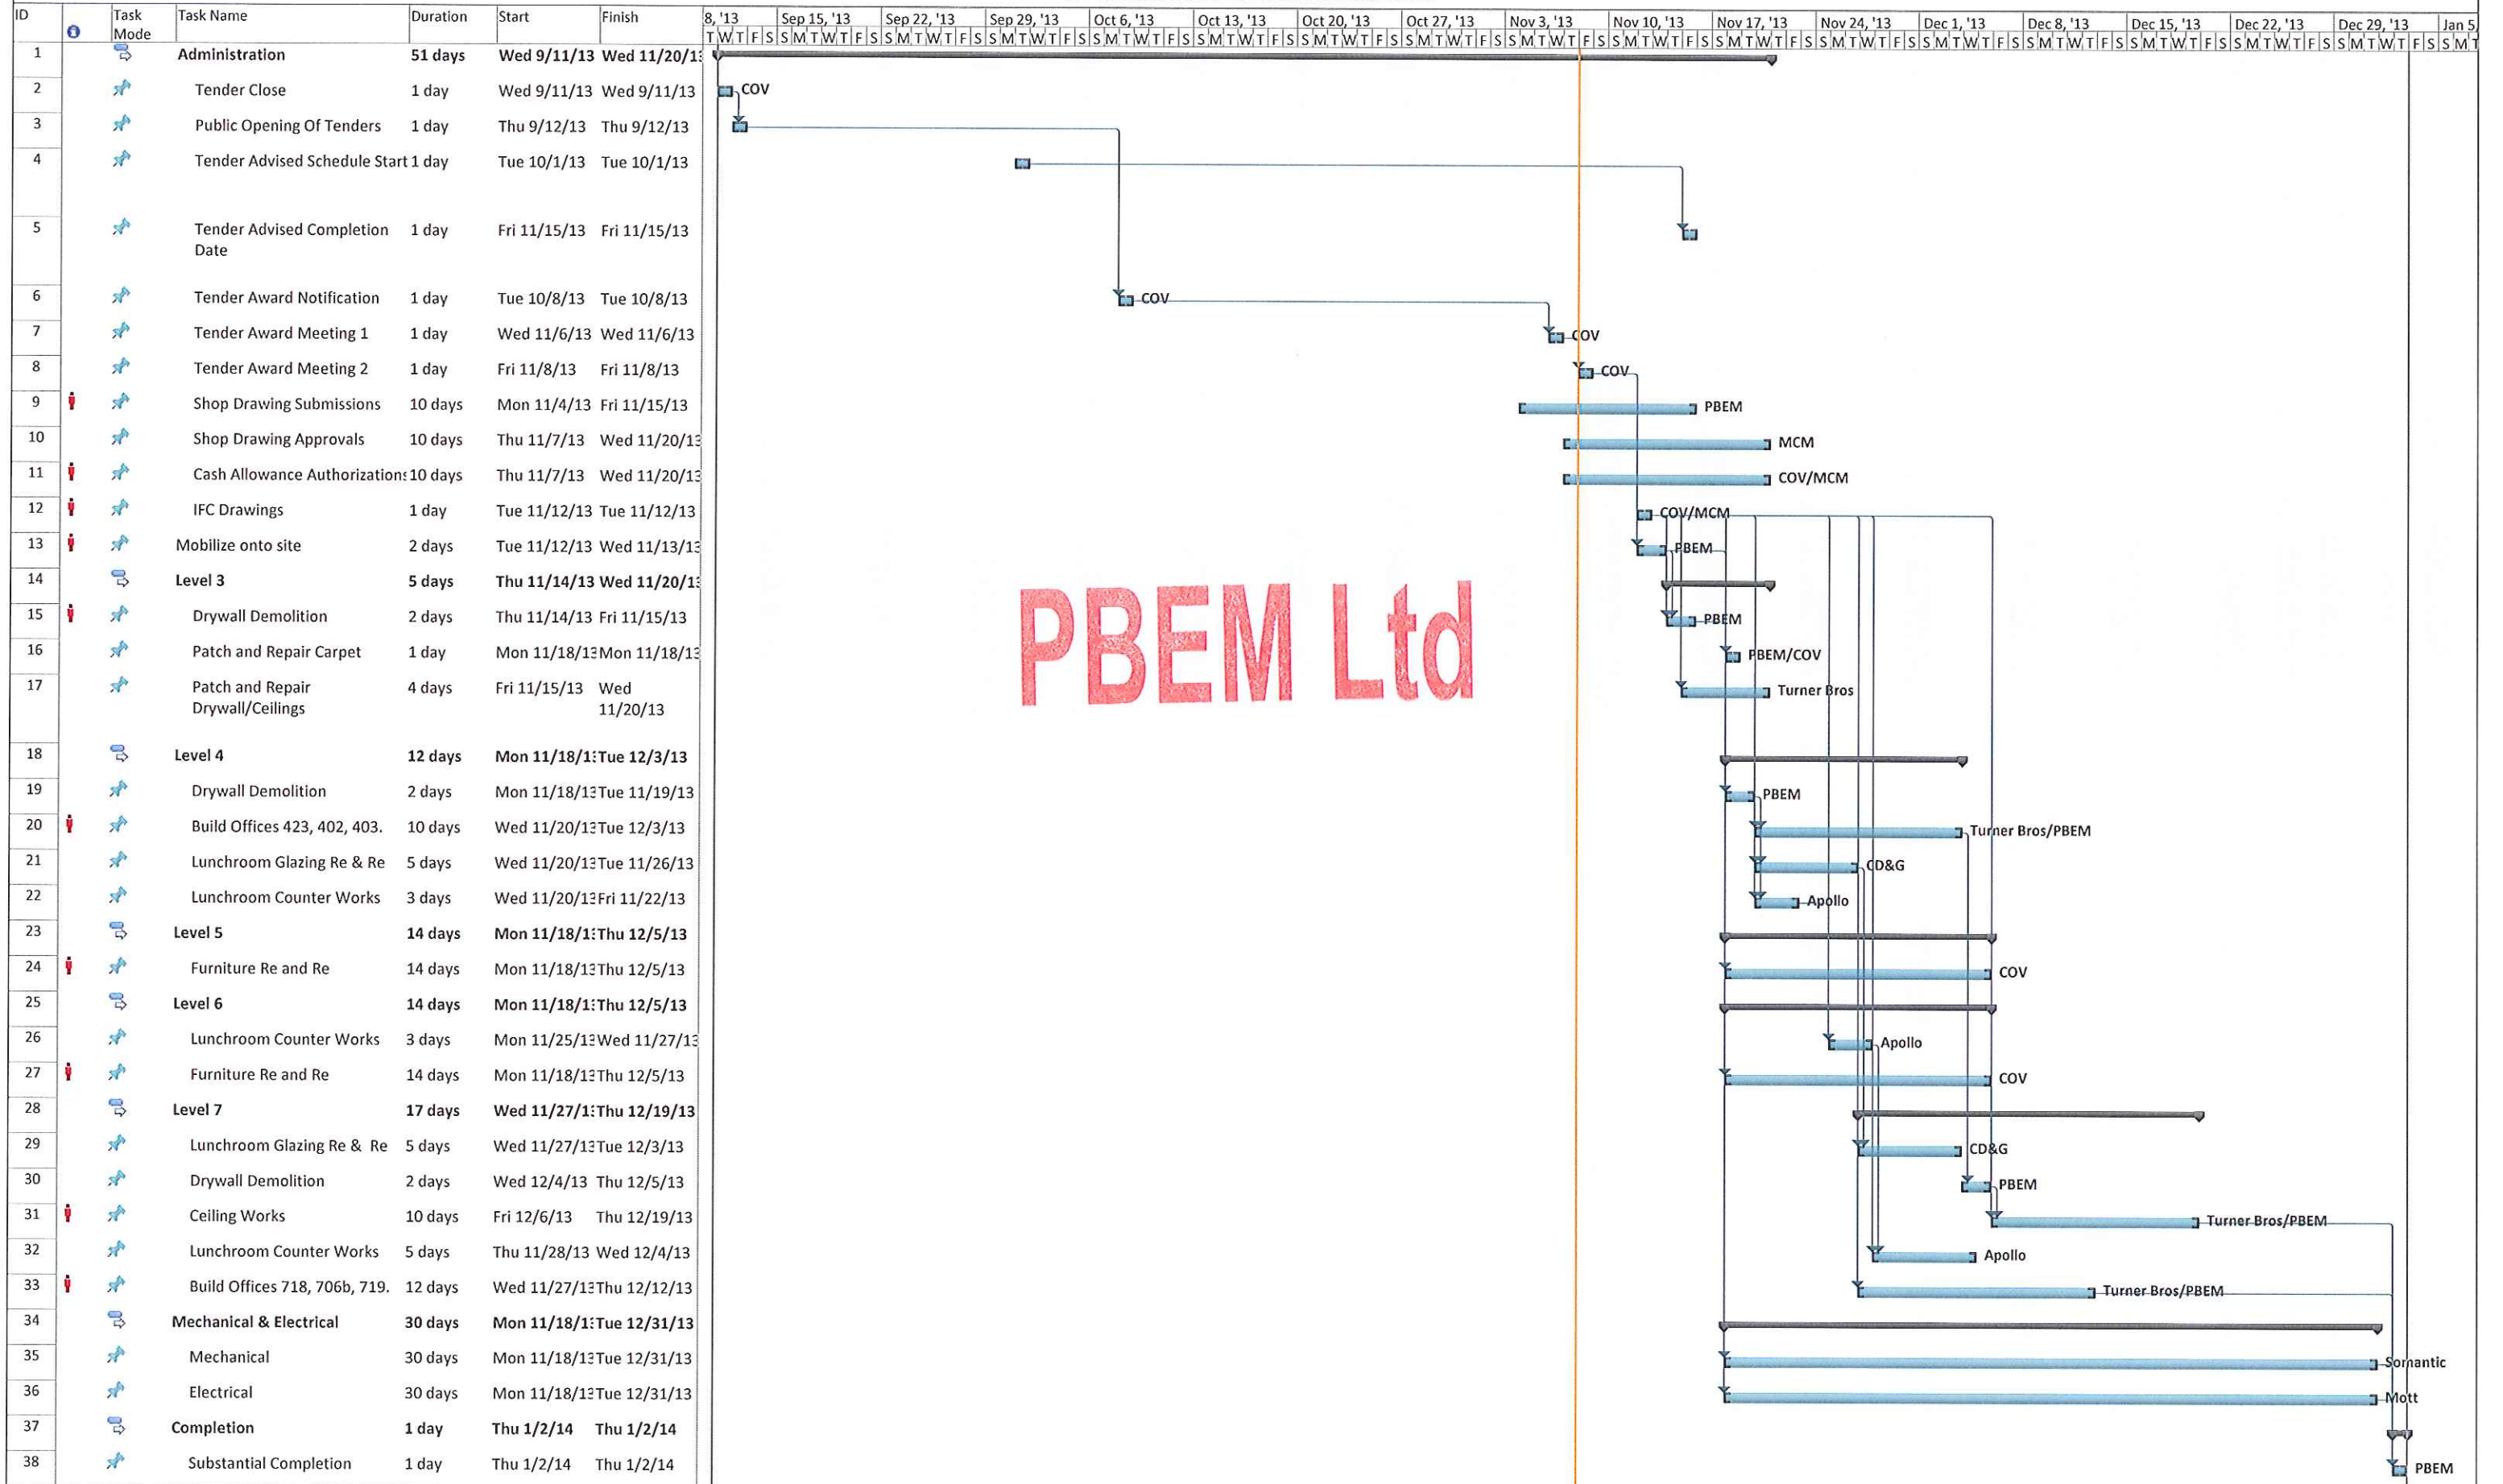

PBEM Ltd

Project: CROSSROADS Baseline Date: Fri 11/8/13	Task	Summary	External Milestone	Inactive Summary	Manual Summary Rollup	Finish-only
	Split	Project Summary	Inactive Task	Manual Task	Manual Summary	Deadline
	Milestone	External Tasks	Inactive Milestone	Duration-only	Start-only	Progress

COV VANCITY Office Renovation BASELINE SCHEDULE

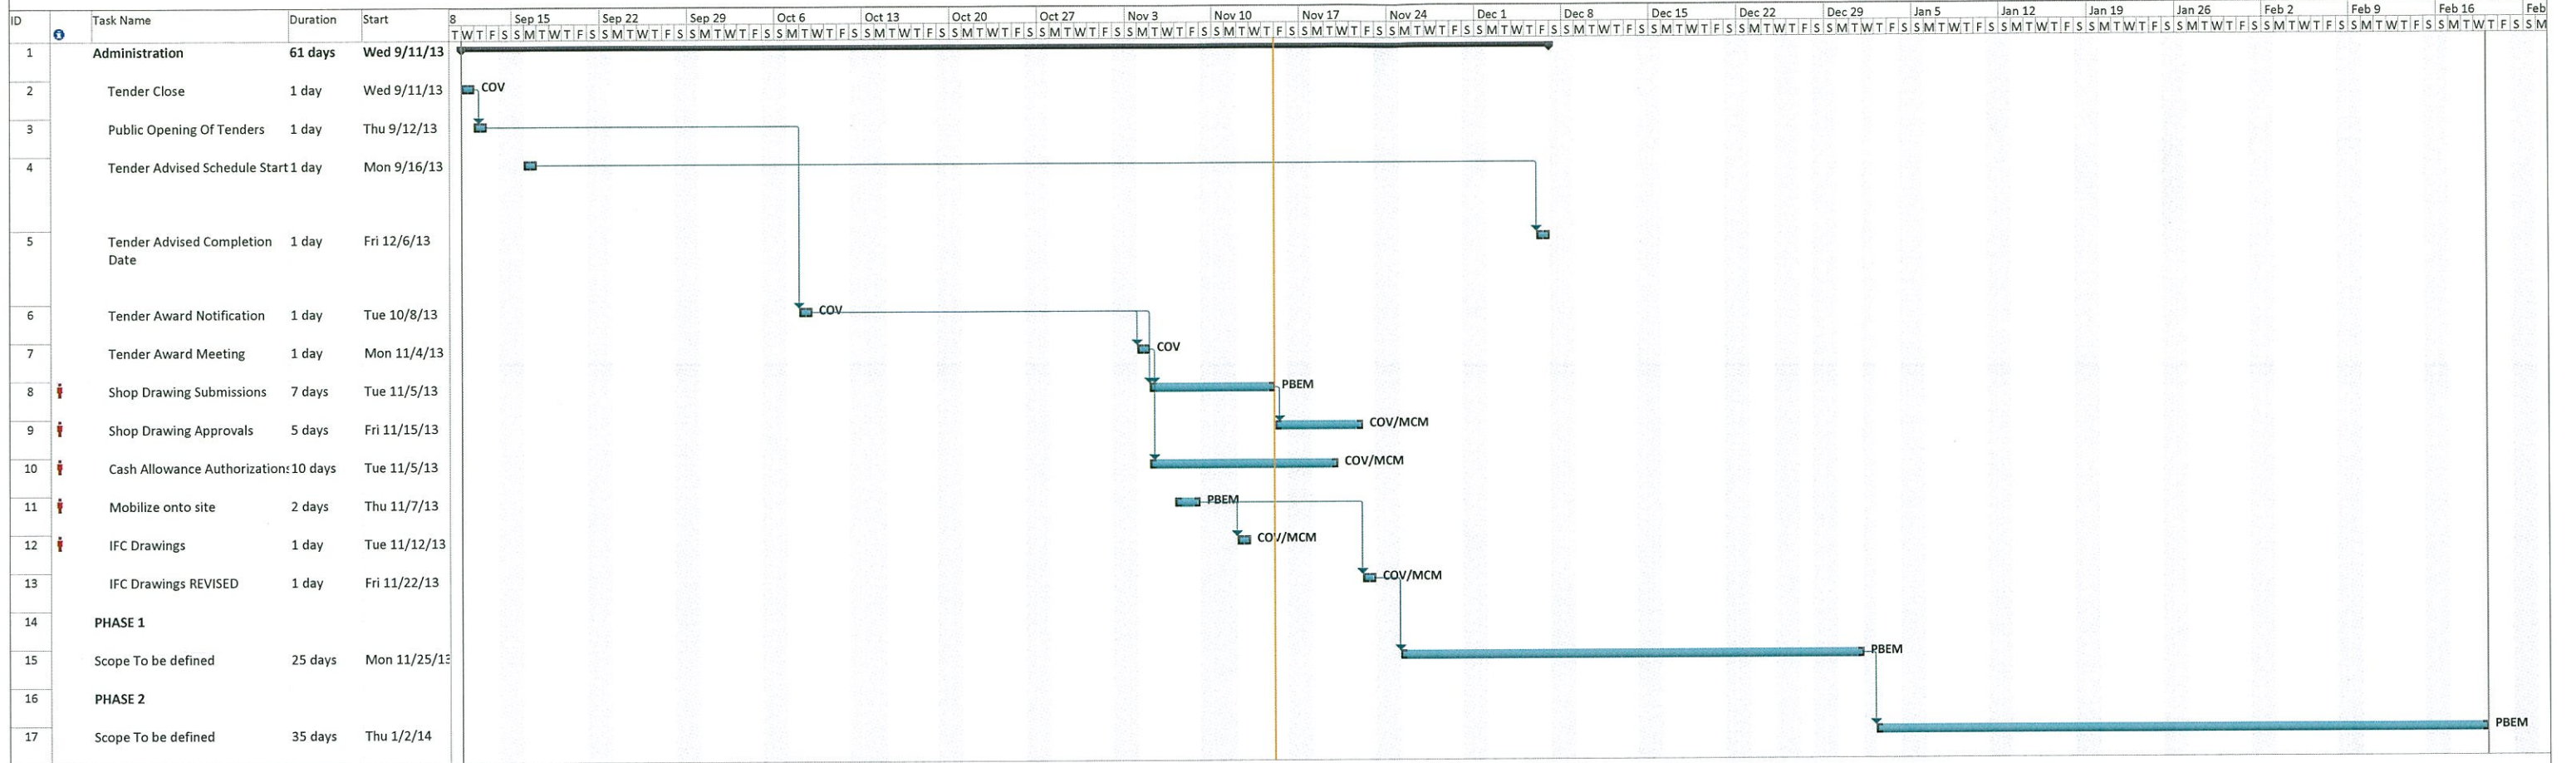

PBEM Ltd

Project: Baseline Date: Fri 11/15/13	Task Split	Milestone Summary	Project Summary External Tasks	External Milestone Inactive Task	Inactive Milestone Inactive Summary	Manual Task Duration-only	Manual Summary Rollup Manual Summary	Start-only Finish-only	Deadline Progress
---	---------------	----------------------	-----------------------------------	-------------------------------------	--	------------------------------	---	---------------------------	----------------------
